STANDARD OPERATING PROCEDURE

Monthly Partner / Donor Reporting

Field	Detail	Field	Detail
SOP code	SOP-OPS-02	Version	1.0
Process owner	M&E Officer	Effective date	1 Nov 2026
Department	Monitoring & Evaluation	Review cycle	Every 6 months
Applies to	All funded programmes	Approved by	Operations Manager

1. Purpose

Deliver an accurate, on-time monthly report to every partner and donor by working day 7, with indicators traceable to source records and data errors below 2%.

2. Scope

- In scope: monthly progress reports on output and outcome indicators for funded programmes.
- Out of scope: annual evaluations and financial reports (handled by Finance).
- Starts at month-end close of attendance data; ends when the partner acknowledges receipt.

3. Definitions

Term	Meaning
Indicator	A measurable result agreed in the results framework (e.g. trainees completing ≥ 80% of sessions).
Source record	Attendance sheet, registration tracker or assessment file the indicator is calculated from.
Data-quality check	Automated and manual checks for duplicates, blanks, impossible values and mismatches with source.
Variance note	Short explanation for any indicator more than 10% off its monthly target.
D+N	N working days after month end.


4. Roles & responsibilities (RACI)

R = Responsible · A = Accountable · C = Consulted · I = Informed

Activity	M&E Officer	Coordinator	Ops Manager	Partner
Close attendance and source data	C	R	A	—
Run data-quality checks	R	C	A	—
Update KPI dashboard	R	I	A	—
Write narrative & variance notes	R	C	A	—
Review and sign-off	C	I	R/A	—
Submit and log feedback	R	I	A	I

5. Process flow

Monthly Partner / Donor Reporting — process flow

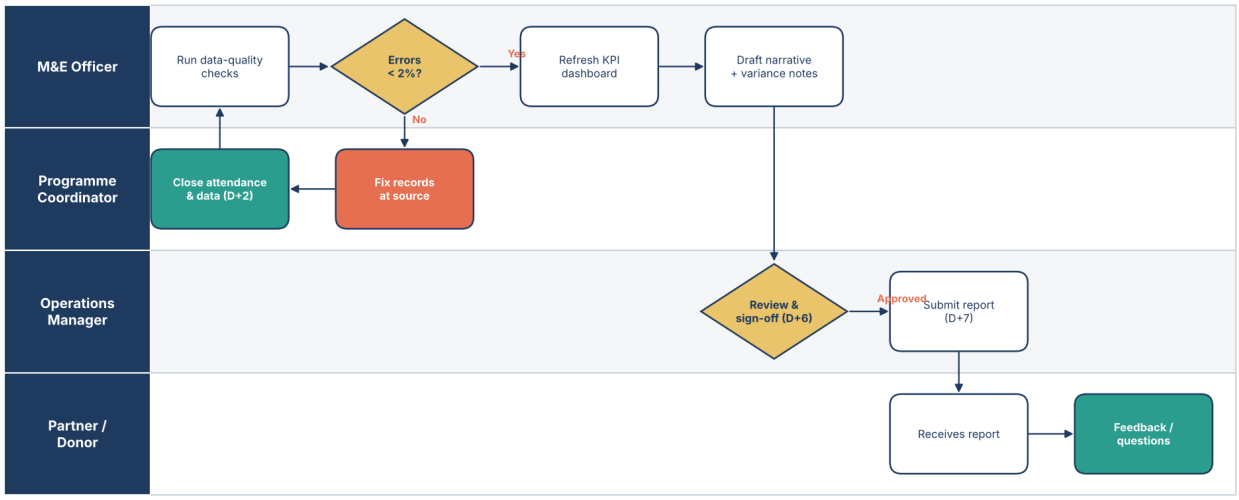

6. Procedure

#	Step	Owner	When	Tool / record	Output
1	Close all attendance sheets and the registration tracker for the month.	Coordinator	D+2	Tracker; attendance files	Locked source data
2	Run the data-quality checklist: duplicates, blanks, out-of-range values, totals vs source.	M&E Officer	D+3	DQ check tab	Error log
3	If errors ≥ 2% of rows, send the error log back and fix at source; re-run checks.	M&E Officer	D+3	Error log	Clean data
4	Refresh the KPI dashboard; compare each indicator with its monthly target.	M&E Officer	D+4	KPI dashboard	Indicator table
5	Write the narrative: achievements, challenges, variance notes for any indicator ±10% off target.	M&E Officer	D+5	Report template	Draft report
6	Review figures against source on a 10% sample; approve or return with comments.	Ops Manager	D+6	Review checklist	Signed-off report
7	Submit to partner portal / email and log the submission.	M&E Officer	D+7	Submission log	Sent report
8	Log partner questions and agree actions for next month.	M&E Officer	D+10	Feedback log	Action list

7. Quality controls

- Every reported number links to a named source file and tab.
- Totals in the report equal totals in the dashboard (automatic reconciliation cell = 0).
- Variance notes are required for any indicator more than 10% off target.
- Two-person rule: preparer and approver are never the same person.

8. Performance indicators

KPI	Target	How it is measured	Frequency	Owner
On-time submission	100% by D+7	Submission date vs deadline	Monthly	M&E Officer
Data error rate	< 2%	Rows failing DQ checks ÷ total rows	Monthly	M&E Officer
Re-submissions	0	Reports returned by partner for corrections	Quarterly	Ops Manager
Feedback closed	100% in 10 days	Partner questions answered ÷ received	Monthly	M&E Officer

9. Exceptions & escalation

Situation	Action	Escalate to	Within
Source data late by > 1 day	Escalate; report on available data with a clear note	Ops Manager	Same day
Indicator off target > 25%	Add root-cause note and recovery plan	Ops Manager	Before D+6
Partner changes template or indicators	Update template and dashboard; confirm in writing	Ops Manager	Next cycle
Data protection concern (personal data)	Remove identifiers; report aggregates only	Ops Manager	Immediately

10. Records & retention

Record	Location	Retention
Monthly report (PDF) + dashboard snapshot	Shared drive /Reports/<partner>/<month>/	Project + 5 years
DQ error log	Same folder	Project + 2 years
Submission & feedback log	M&E tracker	Project + 5 years

11. Related documents

- Results framework and indicator definitions (per partner)
- KPI dashboard template (Excel)
- SOP-OPS-01 Trainee Registration & Onboarding
- Data protection guideline

12. Revision history

Version	Date	Change	Author
0.9	15 Oct 2026	Draft from current reporting cycle	A. H. Dahi
1.0	1 Nov 2026	Added DQ thresholds, two-person rule and checklist	A. H. Dahi

Appendix A — Checklist

Data close (D+2)

- ☐ All attendance sheets received
- ☐ Tracker locked for the month

Quality (D+3)

- ☐ DQ checks run
- ☐ Error rate below 2% or fixed at source

Report (D+4 to D+6)

- ☐ Dashboard refreshed
- ☐ Variance notes written for ±10% indicators
- ☐ 10% sample checked by Ops Manager

Submit (D+7)

- ☐ Report sent and logged
- ☐ Feedback log updated
